

# **Dreams Coming True!**

Get the inside scoop on milestones, perks, and what's ahead at Riverdale Grove.



## Construction Update: April 2025

#### Dear Homeowner,

The vision you believed in is now coming to life!


At Riverdale Grove by Duville Estates, every day brings us closer to delivering the exceptional community you deserve. Crews are hard at work, amenities are taking shape, and your future home is buzzing with energy. In this update, you will find key milestones, insider photos, and what's next.

Thank you for being part of this journey, we can't wait to welcome you home.



### **Residential Tower**

32nd slab 100% RCC work completed, 33rd slab commenced.

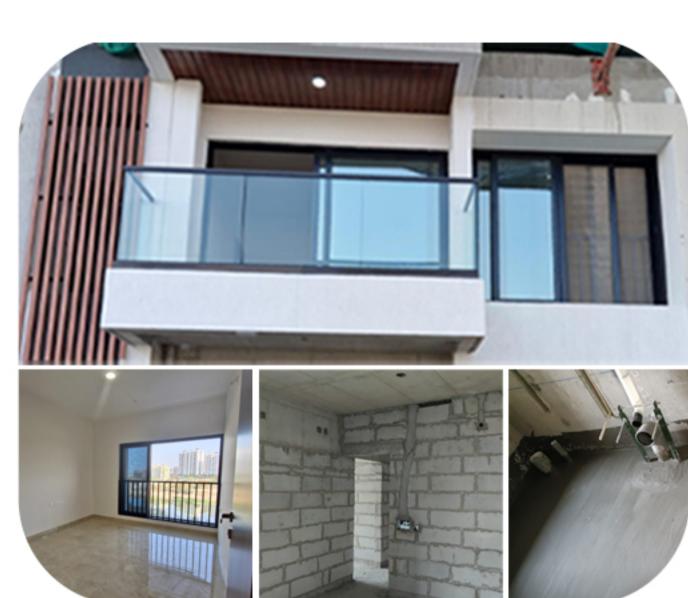

- 27th slab blockwork completed.
- 25th slab gypsum plaster completed; 26th slab work commenced.
- Plumbing work completed up to the 24th slab.
- Waterproofing completed up to the 24th slab.
- Tiling work completed till the 18th slab; 19th and 20th slab tiling work commenced.
- Firefighting work completed up to the 21st slab. • Sliding door and window installation completed till the
- 11th slab; 12th slab work in progress. Cornice work completed up to the 10th slab.
- Balcony texture work completed up to the 15th slab.

## Residential Tower

31st slab 100% RCC work completed, 32nd slab commenced.



- commenced. • 24th slab gypsum plaster completed; 25th slab work
- commenced. • 24th slab waterproofing completed.

25th slab blockwork completed; 26th slab work

• Plumbing work completed up to the 24th slab.

11th slab; 12th slab work in progress.


- Tiling work completed till the 17th slab; 18th and 19th slab tiling work commenced.
- Firefighting work completed up to the 21st slab. Cornice work completed up to the 10th slab.
- Balcony texture work completed up to the 15th slab.

Sliding door and window installation completed till the



# Residential Tower

# 30th slab 50% RCC work completed, 31st slab commenced.

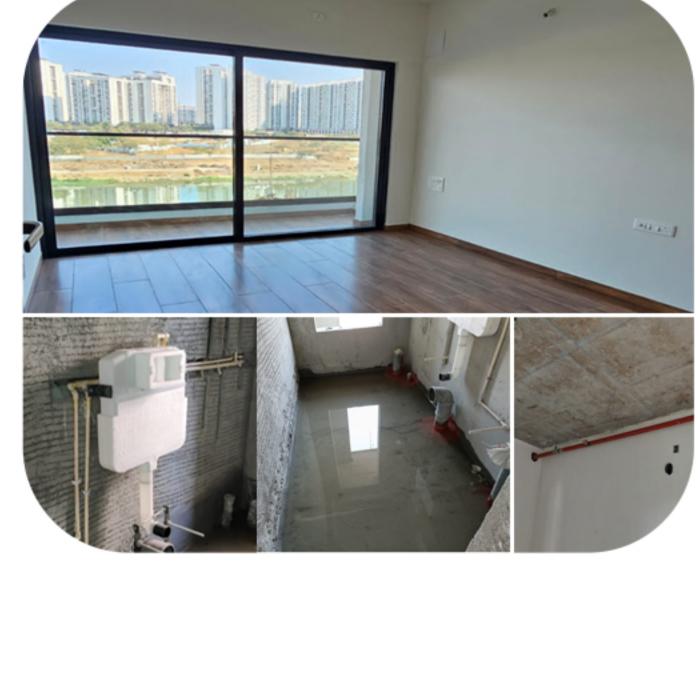

• 23rd slab gypsum plaster completed. • Plumbing work completed up to the 24th slab.

• 23rd slab blockwork completed; 24th slab work

• Waterproofing completed up to the 24th slab.

commenced.


- Tiling work completed till the 17th slab; 18th and 19th slab work commenced.
- Firefighting work completed up to the 21st slab. • Cornice work completed up to the 10th slab.

10th slab; 11th slab work in progress.

• Balcony texture work completed up to the 15th slab.

Sliding door and window installation completed till the

#### Podium Level Waterproofing and hardscape works are currently in progress.

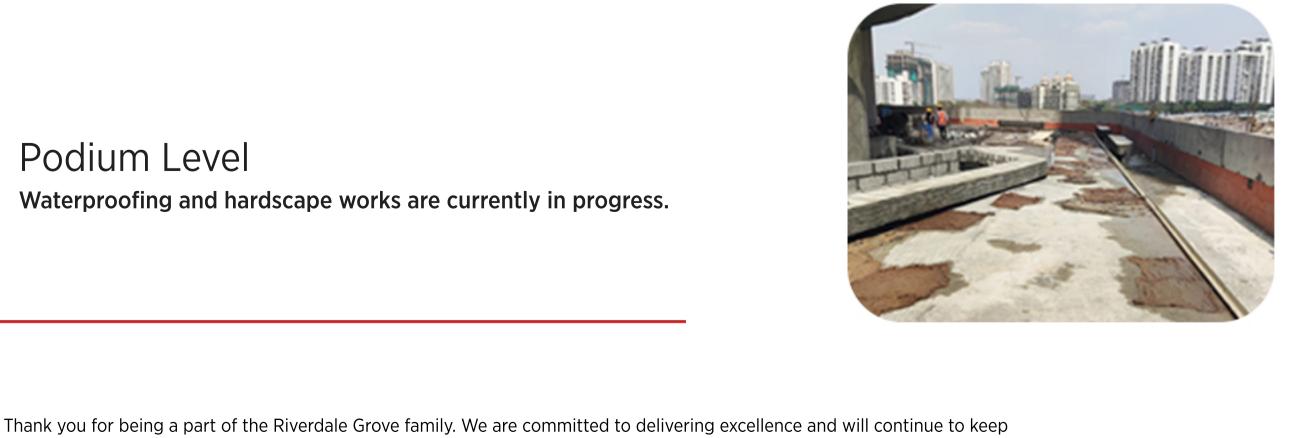

Warm regards, The Riverdale Grove Team

you updated as we reach new milestones.

Riverdale Grove, Plot Bearing / CTS / Survey / Final Plot

S No 16/2A, 17/1, 17/3, 17/4 and 17/5

and actual developments may vary. This is not a legally binding document.

at Kharadi, Haveli, Pune - 411014



info@duville.com





Maha RERA Registration No. P52100029023 https://maharerait.maharashtra.gov.in/

project/view/29414
